Workshop Timeline & Calendar

Trinidad & Tobago Digital Transformation Project

Contract Duration: 12 Months from Contract Signing
Total Workshops: 11
Average Frequency: ~1 workshop per month (some months have 2)

Quick Reference Timeline

```
 YEAR 1 OVERVIEW
═══════════════════════════════════════════════════════════════════════

Q1: DIGITAL FOUNDATIONS
Month 1    Month 2    Month 3
  │          │          │
  WS 1.1     WS 1.2     WS 1.3
  e-ID       Data       Gender &
  Kickoff    Centre     Inclusion

Q2: DIGITAL COLLABORATION
Month 4    Month 5    Month 6
  │          │          │
  WS 2.1     WS 2.2     WS 2.3
  Interop    Regional   Cross-Border
  Standards  Coop       e-ID Pilots

Q3: DIGITAL INNOVATION
Month 7    Month 8    Month 9
  │          │          │
  WS 3.1     WS 3.2     WS 3.3 + 3.4
  Tech Hub   Emerging   Private +
  Launch     Tech       MDA P1

Q4: DIGITAL SUSTAINABILITY
Month 10   Month 11   Month 12
  │          │          │
  WS 4.1     WS 4.2     [Final]
```

```
MDA         Security   Report
Part 2      Governance Period
```

Detailed Monthly Schedule

PHASE 1: DIGITAL FOUNDATIONS

Month 1 - Week 3-4

Workshop 1.1: Digital Identity Ecosystem Kickoff
- **Duration:** 2 days
- **Primary Component:** e-ID Program
- **Key Stakeholders:** MPAAI, 4 ID providers, MDAs, National-CSIRT, 2-3 Caribbean agencies
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 2 - Week 2-3

Workshop 1.2: Data Centre as National Infrastructure
- **Duration:** 1.5 days
- **Primary Component:** Data Centre Expansion
- **Key Stakeholders:** MPAAI, Data Centre team, Infrastructure providers, EU experts
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 3 - Week 2-3

Workshop 1.3: Gender, Inclusion & Digital Rights Foundation
- **Duration:** 1.5 days
- **Primary Component:** Cross-cutting (All)
- **Key Stakeholders:** MPAAI, Civil society, Women's groups, Disability advocates, MDAs
- **Deliverable Link:** Product 3 (Workshop Reports)

End of Q1 Milestone: Product 2 - Technical Progress Analysis 1

PHASE 2: DIGITAL COLLABORATION

Month 4 - Week 3-4

Workshop 2.1: Interoperability Standards & Architecture
- **Duration:** 2 days
- **Primary Component:** Interoperability Platform

- **Key Stakeholders:** MPAAI, MDAs, National-CSIRT, Technical teams, EU experts
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 5 - Week 2-4

Workshop 2.2: Regional Digital Cooperation (Caribbean)
- **Duration:** 2.5 days
- **Primary Component:** Interoperability Platform + e-ID
- **Key Stakeholders:** 2-3 Caribbean country delegations, MPAAI, CAF, EU
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 6 - Week 2-3

Workshop 2.3: Cross-Border e-ID Pilot Design
- **Duration:** 2 days
- **Primary Component:** e-ID Program + Interoperability
- **Key Stakeholders:** MPAAI, Caribbean partners, National-CSIRT, ID providers
- **Deliverable Link:** Product 3 (Workshop Reports) + Product 5 (Pilot Plans)

End of Q2 Milestone: Product 4 - Partial Implementation Report

---

PHASE 3: DIGITAL INNOVATION

Month 7 - Week 2-3

Workshop 3.1: Tech Hub Launch - Open Source & Standards
- **Duration:** 2 days
- **Primary Component:** Data Centre Expansion (Tech Hub #1)
- **Key Stakeholders:** MPAAI, Developer community, Universities, Caribbean partners, EU experts
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 8 - Week 2-3

Workshop 3.2: Emerging Technologies (AI/ML/Blockchain/IoT)
- **Duration:** 2.5 days (spread over 4 days with hands-on time)
- **Primary Component:** Data Centre Expansion (Tech Hub #2-5)
- **Key Stakeholders:** MPAAI, Tech community, Universities, Private sector, International experts
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 9 - Week 2

Workshop 3.3: Private Sector & Third-Party Engagement
- **Duration:** 1.5 days

- **Primary Component:** Data Centre Expansion (Third-party)
- **Key Stakeholders:** Private sector companies, Startups, MPAAI, Legal/compliance experts
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 9 - Week 4

Workshop 3.4: MDA Digital Transformation Showcase (Part 1)
- **Duration:** 1 day
- **Primary Component:** Interoperability Platform + Data Centre (MDA #1)
- **Key Stakeholders:** All MDAs, MPAAI, Early adopters present demos
- **Deliverable Link:** Product 3 (Workshop Reports)

PHASE 4: DIGITAL SUSTAINABILITY

Month 10 - Week 3

Workshop 4.1: MDA Digital Transformation Showcase (Part 2)
- **Duration:** 1 day
- **Primary Component:** Interoperability Platform + Data Centre (MDA #2)
- **Key Stakeholders:** All MDAs, MPAAI, Additional adopters present progress
- **Deliverable Link:** Product 3 (Workshop Reports)

Month 11 - Week 2-3

Workshop 4.2: Security, Ethics & Long-term Governance
- **Duration:** 2 days
- **Primary Component:** All (Integration)
- **Key Stakeholders:** MPAAI, National-CSIRT, Legal experts, All component leads, Private sector
- **Deliverable Link:** Product 3 (Workshop Reports)

End of Q4 Milestone: Product 6 - Final Project Report

Workshop Intensity Heatmap

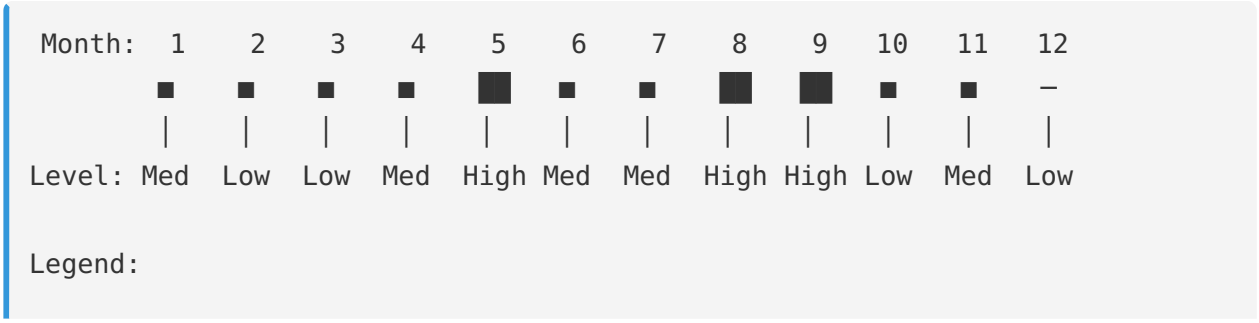

```
—   = No workshop (reporting/planning)
■   = Standard workshop (1-2 days)
██  = Intensive workshop (2+ days or multiple workshops)
```

Parallel Activities Timeline

```
 Workshops run concurrently with other project activities:

═══════════════════════════════════════════════════════════════
Activity Type    Q1        Q2        Q3        Q4
═══════════════════════════════════════════════════════════════
Workshops        3 WS      3 WS      4 WS      2 WS

Pilot Dev        —         Design    Build     Test/Deploy

Procurement      Start     Active    Complete  —

Reporting        Prod 2    Prod 4    —         Prod 6

Contract Mgmt    ████████████████████████████████

Stakeholder      ████████████████████████████████
Engagement

Gender & Incl    ████████████████████████████████
Integration
```

Regional Partner Engagement Windows

Caribbean partner countries should be engaged according to this schedule:

Partner Activity	Timing	Related Workshop
Initial outreach & interest	Month 1	Pre-WS 1.1
First exposure visit	Month 1	WS 1.1 (observers)
Formal partnership discussions	Month 4-5	Pre-WS 2.2

Partner Activity	Timing	Related Workshop
Active collaboration workshop	Month 5	WS 2.2
Pilot design participation	Month 6	WS 2.3
Tech hub knowledge sharing	Month 7	WS 3.1
Replication planning	Month 9-11	WS 3.3, 4.2

EU Expert Engagement Windows

Expertise Area	Primary Engagement	Workshops
e-ID (Estonia model)	Months 1, 6	WS 1.1, 2.3
Interoperability (X-Road)	Months 4-5	WS 2.1, 2.2
Open Source Governance	Month 7	WS 3.1
Data Protection (GDPR)	Months 3, 11	WS 1.3, 4.2
AI Ethics	Month 8	WS 3.2
Gender Digital Inclusion	Month 3	WS 1.3

Critical Path Dependencies

```
WS 1.1 (e-ID Kickoff)
  └→ WS 2.3 (Cross-Border e-ID)
       └→ WS 4.2 (Governance)

WS 1.2 (Data Centre)
  └→ WS 3.1 (Tech Hub Launch)
       └→ WS 3.2 (Emerging Tech)
            └→ WS 3.3 (Private Sector)

WS 2.1 (Interop Standards)
  └→ WS 2.2 (Regional Coop)
       └→ WS 3.4 (MDA Part 1)
```

```
                └─→ WS 4.1 (MDA Part 2)

WS 1.3 (Gender & Inclusion)
  └─→ [Influences ALL subsequent workshops]
```

Key Insight: Delaying any Phase 1 workshop will cascade to dependent workshops in later phases.

Flexibility & Contingency

Buffer Time

- 1-2 week buffers built into schedule between intensive workshops
- Month 12 reserved for final reporting with no workshops scheduled

Contingency Scenarios

If a workshop must be rescheduled:
1. **Phase 1 workshops** - Can shift 1-2 weeks within their month
2. **Phase 2 workshops** - WS 2.2 requires international coordination; book early
3. **Phase 3 workshops** - WS 3.2 is flexible (can be split into multiple sessions)
4. **Phase 4 workshops** - WS 4.2 must complete before Month 11 end for final reporting

If regional partners can't attend specific workshop:
- WS 2.2 is critical - reschedule if necessary
- WS 1.1 and 3.1 are beneficial but not essential for partner attendance

---

Preparation Lead Times

Activity	Lead Time	Notes
Regional partner invitations	6-8 weeks	Visa, travel approvals
EU expert booking	4-6 weeks	Coordinate with EU schedules
Venue booking (large)	4 weeks	For 50+ participants
Venue booking (standard)	2 weeks	For 20-30 participants
Technical setup (labs)	3 weeks	For hands-on workshops

Activity	Lead Time	Notes
Content development	3-4 weeks	Per workshop
Stakeholder invitations (local)	2 weeks	MPAAI, MDAs

Pre-Workshop Checklist Timeline

6-8 Weeks Before:
- Confirm date and venue
- Invite regional/international participants
- Book EU experts

4 Weeks Before:
- Finalize agenda
- Confirm local stakeholder participation
- Begin content development

2 Weeks Before:
- Complete presentation materials
- Arrange technical setup
- Send pre-workshop materials to participants

1 Week Before:
- Final confirmation from all participants
- Technical rehearsal
- Print materials

Post-Workshop Activities Timeline

Week 1 After:
- Gather feedback surveys
- Draft workshop report

Week 2 After:
- Finalize workshop report (Product 3)
- Share with stakeholders
- Begin implementing workshop recommendations

Week 3-4 After:
- Update project plans based on workshop outcomes
- Prepare for next workshop

Reporting Deadlines Aligned to Workshops

Product	Deadline	Linked Workshops
Product 1: Inception Report	Month 1, Week 1	Before WS 1.1
Product 2: Technical Progress 1	End of Month 3	After WS 1.1-1.3
Product 3: Workshop Reports	Ongoing	Within 2 weeks of each workshop
Product 4: Partial Implementation	End of Month 6	After WS 2.1-2.3
Product 5: Pilot Plans	Month 6-7	After WS 2.3
Product 6: Final Report	Month 12	After WS 4.2

Calendar Export Format

For importing into project management tools:

```
 WS 1.1 | Month 1, Week 3-4 | 2 days | e-ID Kickoff
WS 1.2 | Month 2, Week 2-3 | 1.5 days | Data Centre Infrastructure
WS 1.3 | Month 3, Week 2-3 | 1.5 days | Gender & Inclusion
WS 2.1 | Month 4, Week 3-4 | 2 days | Interoperability Standards
WS 2.2 | Month 5, Week 2-4 | 2.5 days | Regional Cooperation
WS 2.3 | Month 6, Week 2-3 | 2 days | Cross-Border e-ID
WS 3.1 | Month 7, Week 2-3 | 2 days | Tech Hub Launch
WS 3.2 | Month 8, Week 2-3 | 2.5 days | Emerging Tech
WS 3.3 | Month 9, Week 2 | 1.5 days | Private Sector
WS 3.4 | Month 9, Week 4 | 1 day | MDA Showcase P1
WS 4.1 | Month 10, Week 3 | 1 day | MDA Showcase P2
WS 4.2 | Month 11, Week 2-3 | 2 days | Security & Governance
```

Document Version: 1.0
Date: September 26, 2026
Last Updated: September 26, 2026
Next Review: Monthly during project execution
